Roadmap for the cities

What the Urban-Flow Toolbox is, what we do together, and when

THE GOAL

By April 2028, each pilot city has its own Urban-Flow Toolbox installed in its municipality and has completed the first implementation round.

This is milestone MS6 of the Grant Agreement (month 28). We get there in four steps.

1 Setup
October – December 2026
We set up the shared test environment

2 Testing window
January – June 2027
You test the tools

3 Feedback
June 2027
You give feedback and choose

4 Implement
mid-2027 to April 2028
You install your own Toolbox

What is the Toolbox?

The Urban-Flow Toolbox is a web portal that brings together all the Urban-Flow components. In one place you connect city data, measure what matters, simulate measures before building them, and decide together with citizens.

The Toolbox architecture in one picture

What you use
Local Digital Twin, e-Participation, dashboards, indicators, AI assistant, administration

Marketplace
Tools for one topic: heat, energy, mobility, air. Here the cities differ.

Shared base
Indicators, rules, data and data sharing. The same for every city.

Your city data
Sensors, open data, city systems, maps

One central login (Keycloak)
One login opens all the tools. Users and roles are set once, in one place.


Data travels from the bottom to the top

1 Collect → 2 Store → 3 Measure → 4 Analyse → 5 Decide

From the architecture to the real Toolbox

↓

The Toolbox in practice

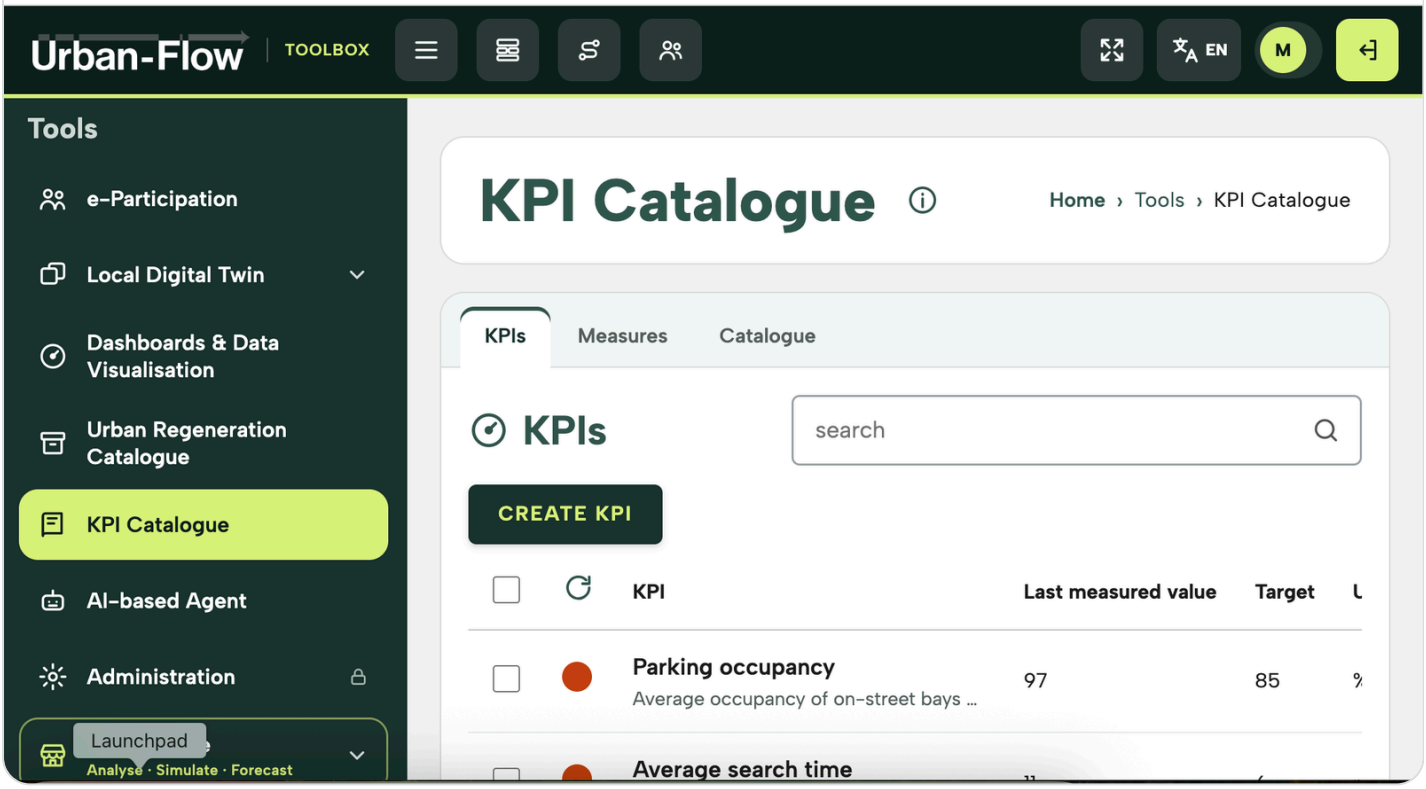

One web portal for all tools

The tools are not separate websites. They are integrated in the Toolbox and open inside the same portal.

One login for all the tools

A single login, managed by a central Keycloak, gives access to every tool.

Same base, different tools

During the testing window there is one shared base for all the cities. On top of it, each city tests the tools that were chosen and assigned to it.

How we get there: four steps

One shared test environment now, and a Toolbox in each city from mid-2027. Click a title to see what is included.

Oct – Dec 2026
M10–M12

STEP 1 **Setup: we set up the shared test environment** — **We are here**

× No installation

WHAT HAPPENS

- ENG and the technical partners build one shared test environment for the three cities. It is installed on servers of the Lisbon Council.
- The test environment opens in January 2027. From January, all the tools are added step by step, starting with the core components.

WHAT YOUR CITY DOES

- **Nothing to install.**
- **Your part: identify the right people in your city and the use cases for the tests. Then the tests can start.**

Who helps: ENG, TEC and the technical partners

Dec 2026
M12

DELIVERABLE **Data tools and collaboration platform, version 1 (D3.3)**

- The first building blocks to manage data, calculate indicators and involve stakeholders.
- They are the base of the shared test environment.

Who is responsible: ENG

Jan – Jun 2027
M13–M18

STEP 2 **Testing window: you test the tools**

× No commitment to adopt a tool **× No installation**

× No daily use in operations

WHAT HAPPENS

- Each city tests a mix of tools, all in the same shared environment:
  - the Marketplace tools the city chose for its own needs;
  - the core components of the architecture;
  - where needed, a few other Marketplace tools. The Grant Agreement asks us to be sure that every tool is tested at least once.

WHAT YOUR CITY DOES

- **Connect your data and play with the Toolbox.**
- **Tell us what you see.**

Tip. Try more than one tool for the same topic. You may discover better alternatives for your final Toolbox.

Who helps: The technical partners support you during the whole testing window

Jun 2027
M18

STEP 3 **Feedback: you give feedback and choose**

WHAT HAPPENS

- Cities tell us what works and what does not, tool by tool.
- Cities and tool owners go through the feedback together. Owners improve their tools.

WHAT YOUR CITY DOES

- **Give your feedback, tool by tool.**
- **Choose: only the tools that met your expectations go to your own Toolbox.**

What you gain. Your feedback improves the tools and helps the Replicant Cities build on what you learn.

Who helps: Tool owners and the technical partners

Jun 2027
M18 · MS4

MILESTONE **First integrated Toolbox (MS4, D3.6)**

- The first version of the Urban-Flow platform, which brings together the first tools and building blocks.

Who is responsible: TEC

Jun 2027 – Apr 2028
M18–M28

STEP 4 **Implement: you install your own Toolbox**

WHAT HAPPENS

- Each city installs its own Toolbox in its own municipality, with the tools that met its expectations.
- There are about 10 months for the local setup and the first implementation round of your pilot.

WHAT YOUR CITY DOES

- **Install your own Toolbox, with the technical partners helping you to configure it.**
- **April 2028 (milestone MS6): your Toolbox is installed, connected to your local data and systems, and the first round of your pilot is described in your pilot implementation report.**

Who helps: The technical partners support you in this phase too

Apr 2028
M28 · MS6

MILESTONE **First implementation round completed (MS6)**

- Each pilot city has installed its own Toolbox and has completed the first round of its pilot.
- Each city describes this first round in its pilot implementation report (D6.3 Valencia, D6.5 Florence, D6.7 Tampere).
- Deliverables due in the same month: the three pilot implementation reports and the Living Labs logbook (D6.1).

Who is responsible: VIC for the milestone, the Valencia report and the logbook; Florence and Tampere for their own reports

We are flexible. The timeline is flexible. What matters: all the tools are tested, and every city has installed its own Toolbox and completed the first implementation round by April 2028.

Key dates for the cities

When	What happens	Who
Oct – Dec 2026	Step 1, Setup: the shared test environment is set up on servers of the Lisbon Council.	ENG · TEC · technical partners
Nov – Dec 2026	Each city identifies the right people and the use cases for the tests.	Cities
Dec 2026	Deliverable D3.3: the data tools and collaboration platform (version 1) is delivered.	ENG
Jan – Jun 2027	Step 2, Testing window: the cities test the tools. From January, all the tools are added step by step, starting with the core components.	Cities · technical partners
Jun 2027	Step 3, Feedback: the cities give feedback and choose.	Cities · tool owners · technical partners
Jun 2027	Milestone MS4: first integrated Toolbox (D3.6).	TEC
Jun 2027 – Apr 2028	Step 4, Implement: each city installs its own Toolbox.	Cities · technical partners
Apr 2028	Milestone MS6: first implementation round completed in each pilot city. Deliverables: the pilot implementation reports (D6.3, D6.5, D6.7) and the Living Labs logbook (D6.1).	VIC · Florence · Tampere

Co-funded by the European Union

Project funded by

www.urban-flow.eu

Urban-Flow **CC-BY 4.0** 2026–2029 Interactive mockup · sample data only

Grant Agreement 101239472 · D3.1 v1
